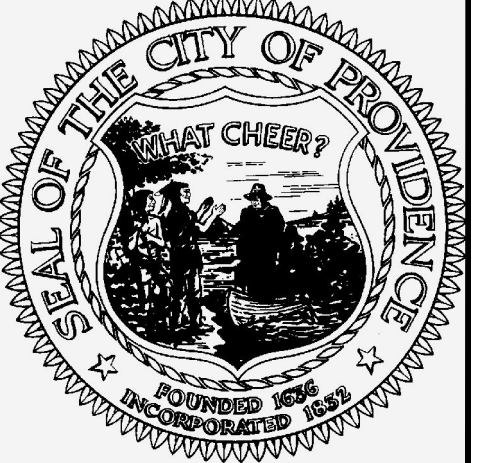


- SEQUENCE OF CONSTRUCTION:**
1. SUBMIT DEWATERING PLAN TO ENGINEER AND RIDEM AT LEAST THIRTY (30) DAYS PRIOR TO MOBILIZATION. CONTRACTOR MAY UTILIZE PLAN BY EA OR MODIFY.
 2. NOTIFY THE ENGINEER AND RIDEM FOR THE REQUIRED PRE-CONSTRUCTION MEETING SEVEN (7) DAYS BEFORE COMMENCING ANY SITE DISTURBANCE.
 3. DIGSAFE ALL UTILITIES PRIOR TO MOBILIZATION.
 4. INSTALL EROSION CONTROLS IN ACCORDANCE WITH SPECIFICATIONS AND BEST MANAGEMENT PRACTICES.
 5. INSTALL STABILIZED CONSTRUCTION ENTRANCES.
 6. CLEAR AND GRUB VEGETATION.
 7. NOTIFY OWNER IF REFUSE REMOVAL OUTSIDE OF SCOPE OF WORK IS NECESSARY.
 8. INSTALL ENGINEERED BARRIER IN SLUICeway.
 9. INSTALL COFFERDAM AS SHOWN IN THE PLANS AND DETAILED IN THE SPECIFICATIONS.
 10. DEWATER THE COFFERDAM AREA OF THE SLUICeway.
 11. GRADE SLUICeway AND INSTALL CHECK DAMS, RELOCATING COFFERDAMS AS NECESSARY.
 12. EXCAVATE WITHIN FLOODPLAIN IN PREPARATION FOR COVER SYSTEMS 1 AND 4.
 13. INSTALL EXCAVATED MATERIAL IN AREA OF COVER SYSTEM 2.
 14. INSTALL GEOTEXTILE ACROSS SITE.
 15. INSTALL 8" OF IMPORTED GRAVEL AS APPROPRIATE.
 16. INSTALL IMPORTED TOPSOIL AS APPROPRIATE.
 17. PLANT SHRUBS, CATTAILS, AND HYDROSEED.
 18. INSTALL EROSION CONTROL MATTING IN AREAS OF PLANTINGS AND BIKE PATH.

SEAL	REVISIONS	DESCRIPTION	
	NO.	DATE	BY
CITY OF PROVIDENCE PARKS DEPARTMENT LINCOLN LACE AND BRAID REMEDIATION PROJECT PROVIDENCE, RHODE ISLAND			
CONSTRUCTION MANAGEMENT PLAN			
 EA ENGINEERING, SCIENCE, AND TECHNOLOGY 2350 Post Road Warwick, Rhode Island 02886 (401) 736-3440			
DATE	MAY 2010		
DESIGNED BY	RGM		
DRAWN BY	DPA		
CHECKED BY	SCM		
PROJECT MANAGER	FBP		
PROJECT NUMBER	61891.05		
SCALE	1" = 40'		
FILE NAME	CONSTRUCTION MANAGEMENT		
DRAWING NUMBER	C-5		
SHEET NUMBER	6 OF 7		
